



INTERNAL SCOPE

Existing Home Renovation

Adelaide Hills, SA



JOB DETAILS	CONTACT
Renovation Prepared by: ScopeSnap Builder Report date: 10/10/2026	Homeowner
Site visit date: 08/10/2026 Inspection marked complete: Yes	5 areas recorded 1 documents attached

OVERVIEW

Renovation of a serviceable but dated South Australian home. Scope based on preliminary visual inspection; verify all quantities and conditions before contracting.

ROOMS & AREAS

Recorded scope and outstanding details are listed together on each room sheet.

01 Kitchen 1 item to confirm	p. 3
02 Main Bathroom 1 item to confirm	p. 5
03 Ensuite 1 item to confirm	p. 7
04 Laundry 1 item to confirm	p. 8
05 Living Room 1 item to confirm	p. 10

SITE ACCESS & NOTES

Existing brick home in serviceable condition. Protect floors and retained windows. Check access, existing services and any concealed conditions before pricing.

BY OWNER

Owner to confirm appliance models and colour selections.



Project notes – continued

OFFICE NOTES

Kitchen, main bathroom and laundry refurbishment; existing rooms remain within the current footprint.

ATTACHED DOCUMENTS

– Existing measured floor plan.jpg

APPROXIMATE QUANTITIES FOR ESTIMATING

Gross dimensions only. No openings, deductions, waste or construction tolerances allowed.

ROOM	FLOOR / WALLS (M ²)
Kitchen	Floor 15.96 m ² · Walls 43.20 m ²
Main Bathroom	Floor 7.44 m ² · Walls 29.70 m ²
Ensuite	Floor 4.14 m ² · Walls 22.14 m ²
Laundry	Floor 5.25 m ² · Walls 24.84 m ²
Living Room	Floor 21.00 m ² · Walls 49.68 m ²
TOTAL (gross)	Floor 53.79 m ² · Walls 169.56 m ² (measured heights only)




ROOM 01 / EXISTING ROOM

Kitchen

SCOPE SUMMARY

- Protect adjacent finishes, disconnect services, and remove existing cupboards, benchtop and tiled splashback.
- Allow new joinery, stone worktop, tiling, plumbing and electrical changes.

PHOTOS

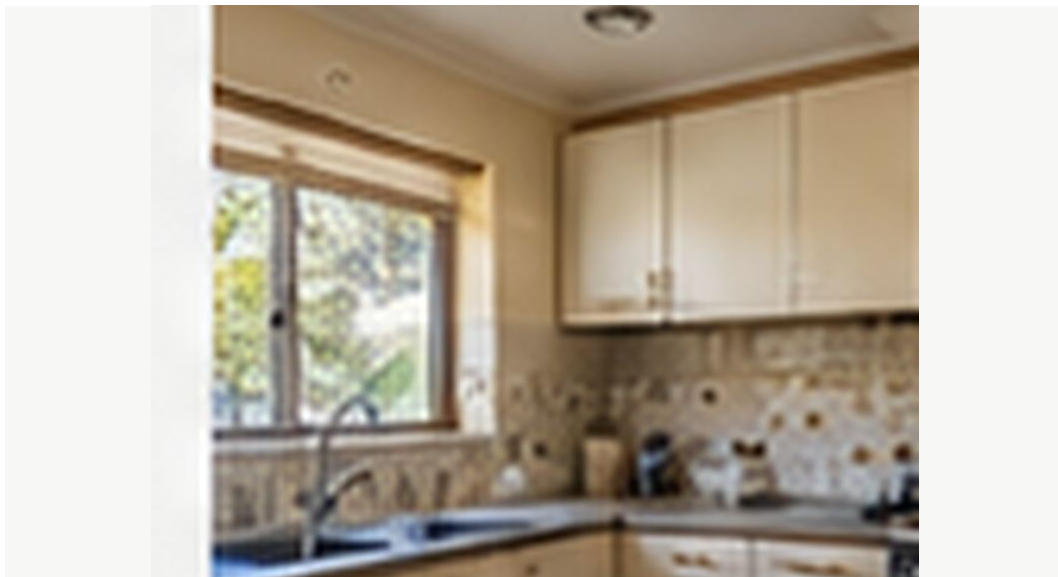

R1-01 / Kitchen — Original kitchen with laminate cupboards, tiled splashback and existing sink under the window.

RECORDED SCOPE & SELECTIONS

ITEM	RECORDED DETAIL
Is the kitchen layout changing	Change within this room
What cabinetry work is required	Replace all cabinetry
Cabinet door style	Shaker
Cabinet finish	Laminate
Benchtop work	Replace
Benchtop material	Stone



Kitchen – continued

ITEM	RECORDED DETAIL
Splashback material	Tiles
Sink	Stainless steel
Tapware	Mixer
Appliances	Oven, Induction cooktop, Dishwasher
Floor finish	Tiles
Island bench	Yes
Plumbing work required	Yes
Electrical work required	Yes
Lighting	Downlights, Pendants

BY OWNER

- Kitchen appliances.

MEASUREMENTS

- Length (m): 4.2
- Width (m): 3.8
- Ceiling height (m): 2.7

Floor area: 15.96 m² (length x width; no waste allowance).

TO CONFIRM

- Site measurements, appliance schedule, concealed plumbing, switch positions and substrate condition.




ROOM 02 / EXISTING ROOM

Main Bathroom

SCOPE SUMMARY

- Full strip-out of fixtures and tiles.
- Renew waterproofing and plumbing rough-in as required, tile and fit new vanity/shower.

PHOTOS

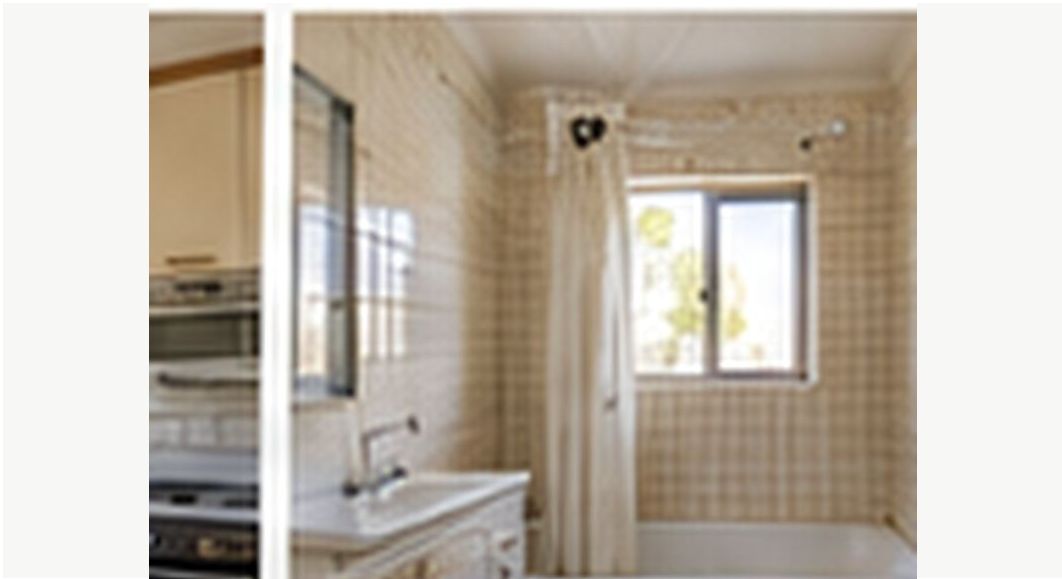

R2-01 / Main Bathroom — Existing bathroom with older tiled walls, bath and shower fittings.

RECORDED SCOPE & SELECTIONS

ITEM	RECORDED DETAIL
Bath	No bath
Shower screen	Semi-frameless
Shower niche	Yes
Vanity	Wall-hung
Vanity top	Stone
Floor finish	Tiles



Main Bathroom – continued

ITEM	RECORDED DETAIL
Shower head	Wall-mounted

MEASUREMENTS

- Length (m): 3.1
 - Width (m): 2.4
 - Ceiling height (m): 2.7
- Floor area: 7.44 m² (length x width; no waste allowance).

TO CONFIRM

- Shower screen measurement, ventilation and substrate repairs.



ROOM 03 / EXISTING ROOM

Ensuite

SCOPE SUMMARY

- Replace nominated ensuite finishes and fittings.

PHOTOS



R3-01 / Ensuite — Original ensuite with older sanitaryware and tiled walls.

MEASUREMENTS

- Length (m): 2.3
 - Width (m): 1.8
 - Ceiling height (m): 2.7
- Floor area: 4.14 m² (length x width; no waste allowance).

TO CONFIRM

- Waterproofing and drainage positions.



ROOM 04 / EXISTING ROOM

Laundry

SCOPE SUMMARY

- Remove trough, joinery and tiled finishes; replace cabinetry and worktop.

PHOTOS



R4-01 / Laundry — Serviceable original laundry with older cabinet, tile splashback and exterior door.

RECORDED SCOPE & SELECTIONS

ITEM	RECORDED DETAIL
What cabinetry work is required	Replace all cabinetry
Benchtop work	Replace
Benchtop material	Laminate
Laundry trough	Stainless steel
Washer / dryer setup	Side by side
Floor finish	Tiles



Laundry – continued

MEASUREMENTS

- Length (m): 2.5
 - Width (m): 2.1
 - Ceiling height (m): 2.7
- Floor area: 5.25 m² (length x width; no waste allowance).

TO CONFIRM

- Existing washer and trough services.



ROOM 05 / EXISTING ROOM

Living Room

SCOPE SUMMARY

- Preparation, painting and floor finish replacement.

PHOTOS



R5-01 / Living Room — Existing living room with dated finishes and sliding glass door to backyard.

MEASUREMENTS

- Length (m): 5.0
- Width (m): 4.2
- Ceiling height (m): 2.7

Floor area: 21.00 m² (length x width; no waste allowance).

TO CONFIRM

- Retain existing door and window openings.



PHOTO RECORD

Site photos

PHOTOS



SITE-01 / Site — Existing brick veneer facade and tiled roof, with mature garden retained.
